



**MS/HS Summer 2021 Improvement List:**


- Mechanical/HVAC Work:
  - HS Classroom Unit Ventilators and Painted Ceilings
  - MS AHU 1, 2, 3 Refurbishment and VAV Replacement
  - MS AHU 4, 5, 6 Refurbishment and VAV Replacement
  - MS AHU 7, 8, 9 AHU and VAV Refurbishment. Add Cooling to North Gym
  - MS AHU-10 and VAV Replacement
  - MS AHU 11, 12 Replacement and adding cooling (Gym)
  - Chiller & Chilled Pump Replacement
  - HS Cabinet Unit Heater & Baseboard Heating
  - Kitchen Exhaust Fan / Hood and Kitchen Roof Replacement
  - High School Restroom Renovations / Finish Upgrades
  - HS Corridor Ceiling Replacement
  - HS Corridor Flooring Replacement
  - Existing Kitchen Front Serving Line Remodel
  - Classrooms 3210 & 3241 – Remove Storage rooms and finish upgrades
  - HS Divider Walls & Track Removal (Culinary Arts and Econ Classrooms)
  - Add Windows to Econ Classrooms

(Red items were not part of the original estimate)


- Budget: \$ 5,000,000
- Actual Cost: \$ 4,765,509



Floor Finish Replacement

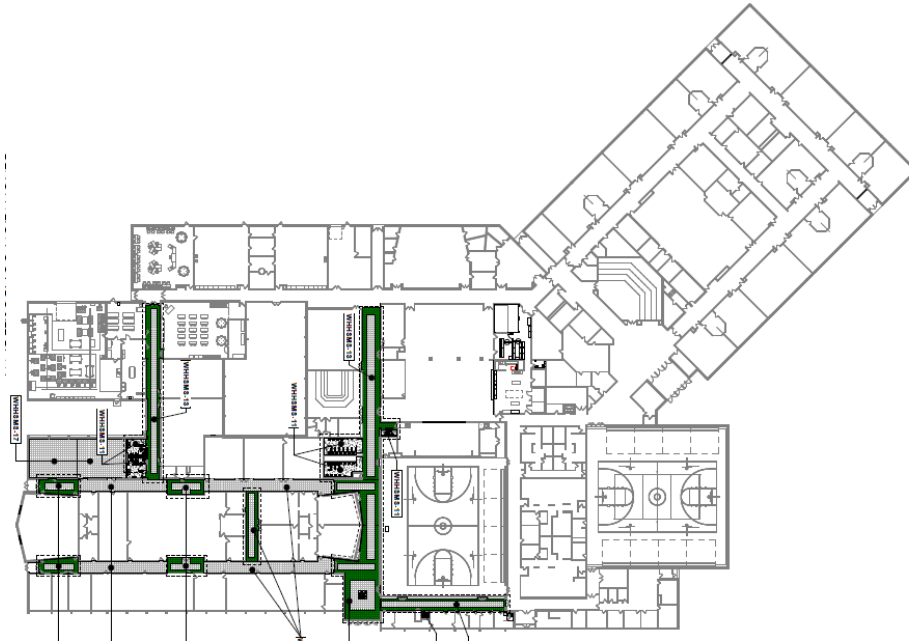

Renovation Scope of Work

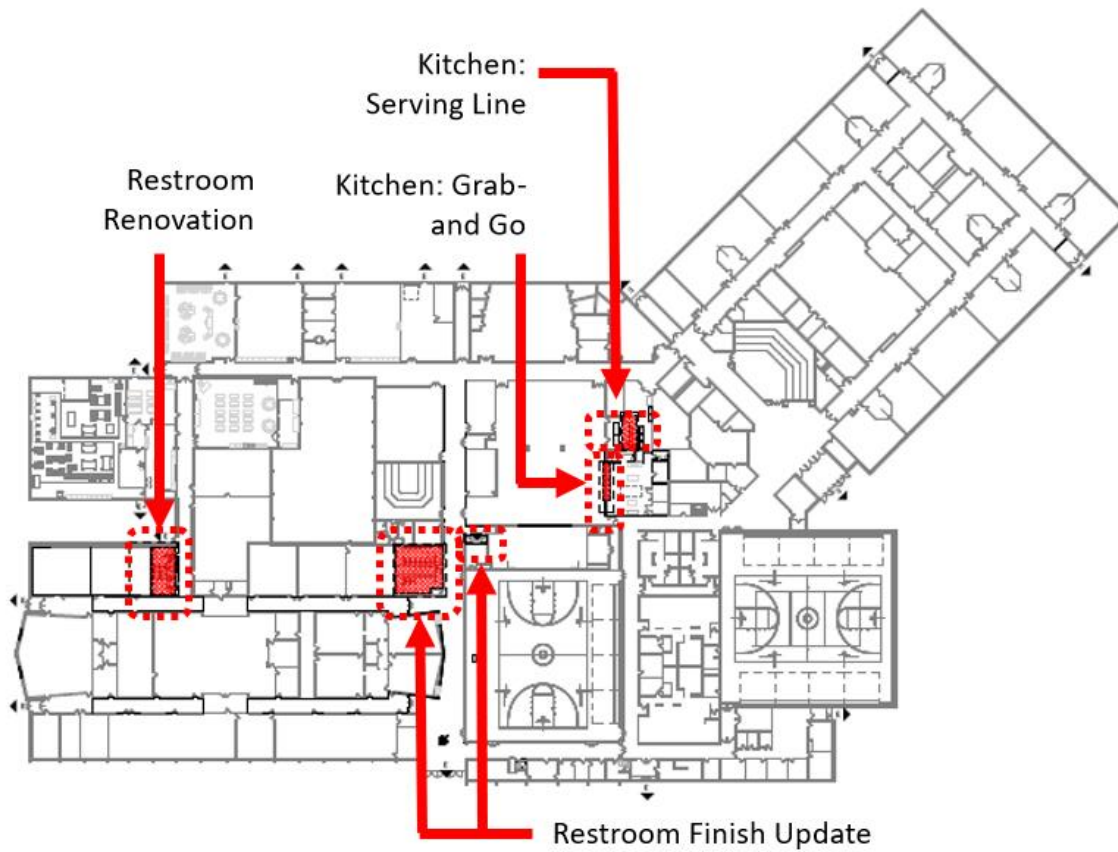



**Design Update:**

- Traffic Impact Study has been submitted to the WisDOT (Complete report after the initial Traffic Study)
- Cloud Ceilings Update
- Exterior Rendering

**Schedule Update: Upcoming Tasks**

- Room-by-room review of Elementary School upcoming
- Pricing of Elementary School
- April Board Meeting rendering of High School entrance.
- Rendering of the existing kitchen / cafeteria

**Rendering Updates:**

WWS



*Exterior*



*Exterior from North*



*Vestibule*





*Media Center*



*Gymnasium*



Art Room

Corridor Design:



jim








*Color at Intersections*

Sample Images of Cloud Ceilings

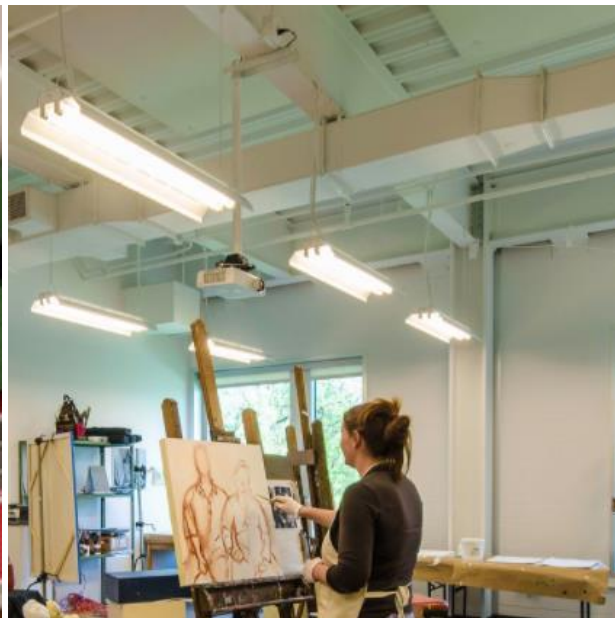





Wisconsin Heights  
High School Renovation  
Elementary School Addition

March 22, 2021  
Project Update

